


MANSFIELD UNIVERSITY - LIGHTING RETROFIT INSTALLATION SCHEDULE

ID	Task Name	Duration	Start	Finish	Predecessors	January			February			March			April	
						B	M	E	B	M	E	B	M	E	B	M
1	MANSFIELD UNIVERSITY LIGHTING SCHEDULE	170.75 days	Mon 2/2/09	Fri 1/15/10												
2	Submittal Process	5 days	Mon 2/2/09	Tue 2/10/09												
3	Product Procurement	20 days	Tue 2/10/09	Mon 3/23/09	2											
4	Mobilization	5 days	Mon 3/23/09	Wed 4/1/09	3											
5	Lighting Installation	130.75 days	Wed 4/1/09	Mon 12/28/09												
6	Doane Center/University Police	3.5 days	Wed 4/1/09	Wed 4/8/09	4											
7	Alumni House	0.75 days	Wed 4/8/09	Thu 4/9/09	6											
8	Beecher House	0.75 days	Thu 4/9/09	Mon 4/13/09	7											
9	Alumni Hall/Student Center	5 days	Mon 4/13/09	Wed 4/22/09	8											
10	Manser Hall	4 days	Thu 4/23/09	Thu 4/30/09	9											
11	Pinecrest Manor	5.5 days	Mon 5/4/09	Wed 5/13/09	10											
12	Laurel Manor "A"	6 days	Wed 5/13/09	Wed 5/27/09	11											
13	Laurel Manor "B"	3.75 days	Wed 5/27/09	Thu 6/4/09	12											
14	Maple Hall "A"	9.75 days	Thu 6/4/09	Thu 6/25/09	13											
15	Maple Hall "B"	4 days	Thu 6/25/09	Mon 7/6/09	14											
16	Decker Gymnasium (Gym Floor)	6 days	Mon 7/6/09	Thu 7/16/09	15											
17	Rod Kelchner Fitness Center (Gym Floor)	6 days	Thu 7/16/09	Thu 7/30/09	16											
18	Cedarcrest Hall "A"	5 days	Thu 7/30/09	Tue 8/11/09	17											
19	Cedarcrest Hall "B"	5.25 days	Tue 8/11/09	Mon 8/24/09	18											
20	Decker Gymnasium	7.5 days	Mon 8/24/09	Wed 9/9/09	19											
21	Rod Kelchner Fitness Center	5 days	Wed 9/9/09	Mon 9/21/09	20											
22	Butler Center	3 days	Mon 9/21/09	Mon 9/28/09	21											
23	Steadman Theater	4 days	Mon 9/28/09	Mon 10/5/09	22											
24	Fieldhouse	1 day	Mon 10/5/09	Tue 10/6/09	23											
25	Memorial Hall	5 days	Tue 10/6/09	Wed 10/14/09	24											
26	North Hall	9 days	Wed 10/14/09	Fri 10/30/09	25											
27	Grant Science Center	7 days	Fri 10/30/09	Wed 11/11/09	26											
28	Elliott Hall	6 days	Wed 11/11/09	Mon 11/23/09	27											
29	Straughn Hall	2 days	Mon 11/23/09	Wed 11/25/09	28											
30	Belknap Hall	4 days	Wed 11/25/09	Fri 12/4/09	29											
31	Retan Center	6 days	Fri 12/4/09	Wed 12/16/09	30											
32	Boiler Plant/Carpenter Shop	2 days	Wed 12/16/09	Fri 12/18/09	31											
33	Brooks Maintenance	3 days	Fri 12/18/09	Thu 12/24/09	32											
34	Child Care Center	0.5 days	Thu 12/24/09	Mon 12/28/09	33											
35	Water Plant	0.5 days	Mon 12/28/09	Mon 12/28/09	34											

Schedule: 01 - 32mh, 32mh, 16mh Date: Thursday, January 08, 2009 Work Week: Monday thru Thursday	Task Milestone	External Tasks
Split	Summary	External MileTask
Progress	Project Summary	Split

MANSFIELD UNIVERSITY - LIGHTING RETROFIT INSTALLATION SCHEDULE


ID	Task Name	Duration	Start	Finish	Predecessors	January			February			March			April	
						B	M	E	B	M	E	B	M	E	B	M
36	Punch List	5 days	Mon 12/28/09	Thu 1/7/10	35											
37	Lighting Project Close-Out	5 days	Thu 1/7/10	Fri 1/15/10	36											
38	MANSFIELD UNIVERSITY WEATHERIZATION SCHE	56 days	Mon 2/9/09	Thu 6/4/09												
39	Submittal Process	5 days	Mon 2/9/09	Tue 2/17/09												
40	Product Procurement	10 days	Tue 2/17/09	Mon 3/9/09	39											
41	Mobilization	5 days	Mon 3/9/09	Wed 3/18/09	40											
42	Weatherization	32 days	Thu 3/19/09	Wed 5/27/09												
43	Decker Gymnasium	1 day	Thu 3/19/09	Mon 3/23/09	41											
44	Rod Kelchner Fitness Center	1 day	Mon 3/23/09	Tue 3/24/09	43											
45	Butler Center	1 day	Tue 3/24/09	Wed 3/25/09	44											
46	Steadman Theater	1 day	Wed 3/25/09	Thu 3/26/09	45											
47	Doane Center/University Police	1 day	Mon 3/30/09	Tue 3/31/09	46											
48	Manser Hall	1 day	Tue 3/31/09	Wed 4/1/09	47											
49	Alumni Hall/Student Center	1 day	Wed 4/1/09	Thu 4/2/09	48											
50	Memorial Hall	1 day	Thu 4/2/09	Mon 4/6/09	49											
51	North Hall	5 days	Tue 4/7/09	Thu 4/16/09	50											
52	Grant Science Center	1 day	Thu 4/16/09	Mon 4/20/09	51											
53	Elliott Hall	8 days	Mon 4/20/09	Wed 5/6/09	52											
54	Straughn Hall	1 day	Wed 5/6/09	Thu 5/7/09	53											
55	Belknap Hall	1 day	Thu 5/7/09	Mon 5/11/09	54											
56	Retan Center	1 day	Tue 5/12/09	Wed 5/13/09	55											
57	Pinecrest Manor	1 day	Wed 5/13/09	Thu 5/14/09	56											
58	Laurel Manor "A"	1 day	Thu 5/14/09	Mon 5/18/09	57											
59	Laurel Manor "B"	1 day	Mon 5/18/09	Tue 5/19/09	58											
60	Maple Hall "A"	1 day	Wed 5/20/09	Thu 5/21/09	59											
61	Maple Hall "B"	1 day	Thu 5/21/09	Mon 5/25/09	60											
62	Cedarcrest Hall "A"	1 day	Mon 5/25/09	Tue 5/26/09	61											
63	Cedarcrest Hall "B"	1 day	Tue 5/26/09	Wed 5/27/09	62											
64	Punch List	2 days	Thu 5/28/09	Tue 6/2/09	63											
65	Weatherization Project Close-Out	2 days	Tue 6/2/09	Thu 6/4/09	64											

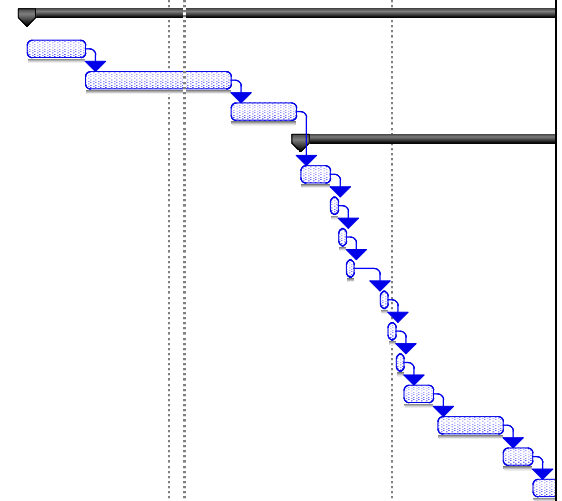

Schedule: 01 - 32mh, 32mh, 16mh
 Date: Thursday, January 08, 2009
 Work Week: Monday thru Thursday

Task		Milestone		External Tasks	
Split		Summary		External MileTask	
Progress		Project Summary		Split	

MANSFIELD UNIVERSITY - LIGHTING RETROFIT INSTALLATION SCHEDULE

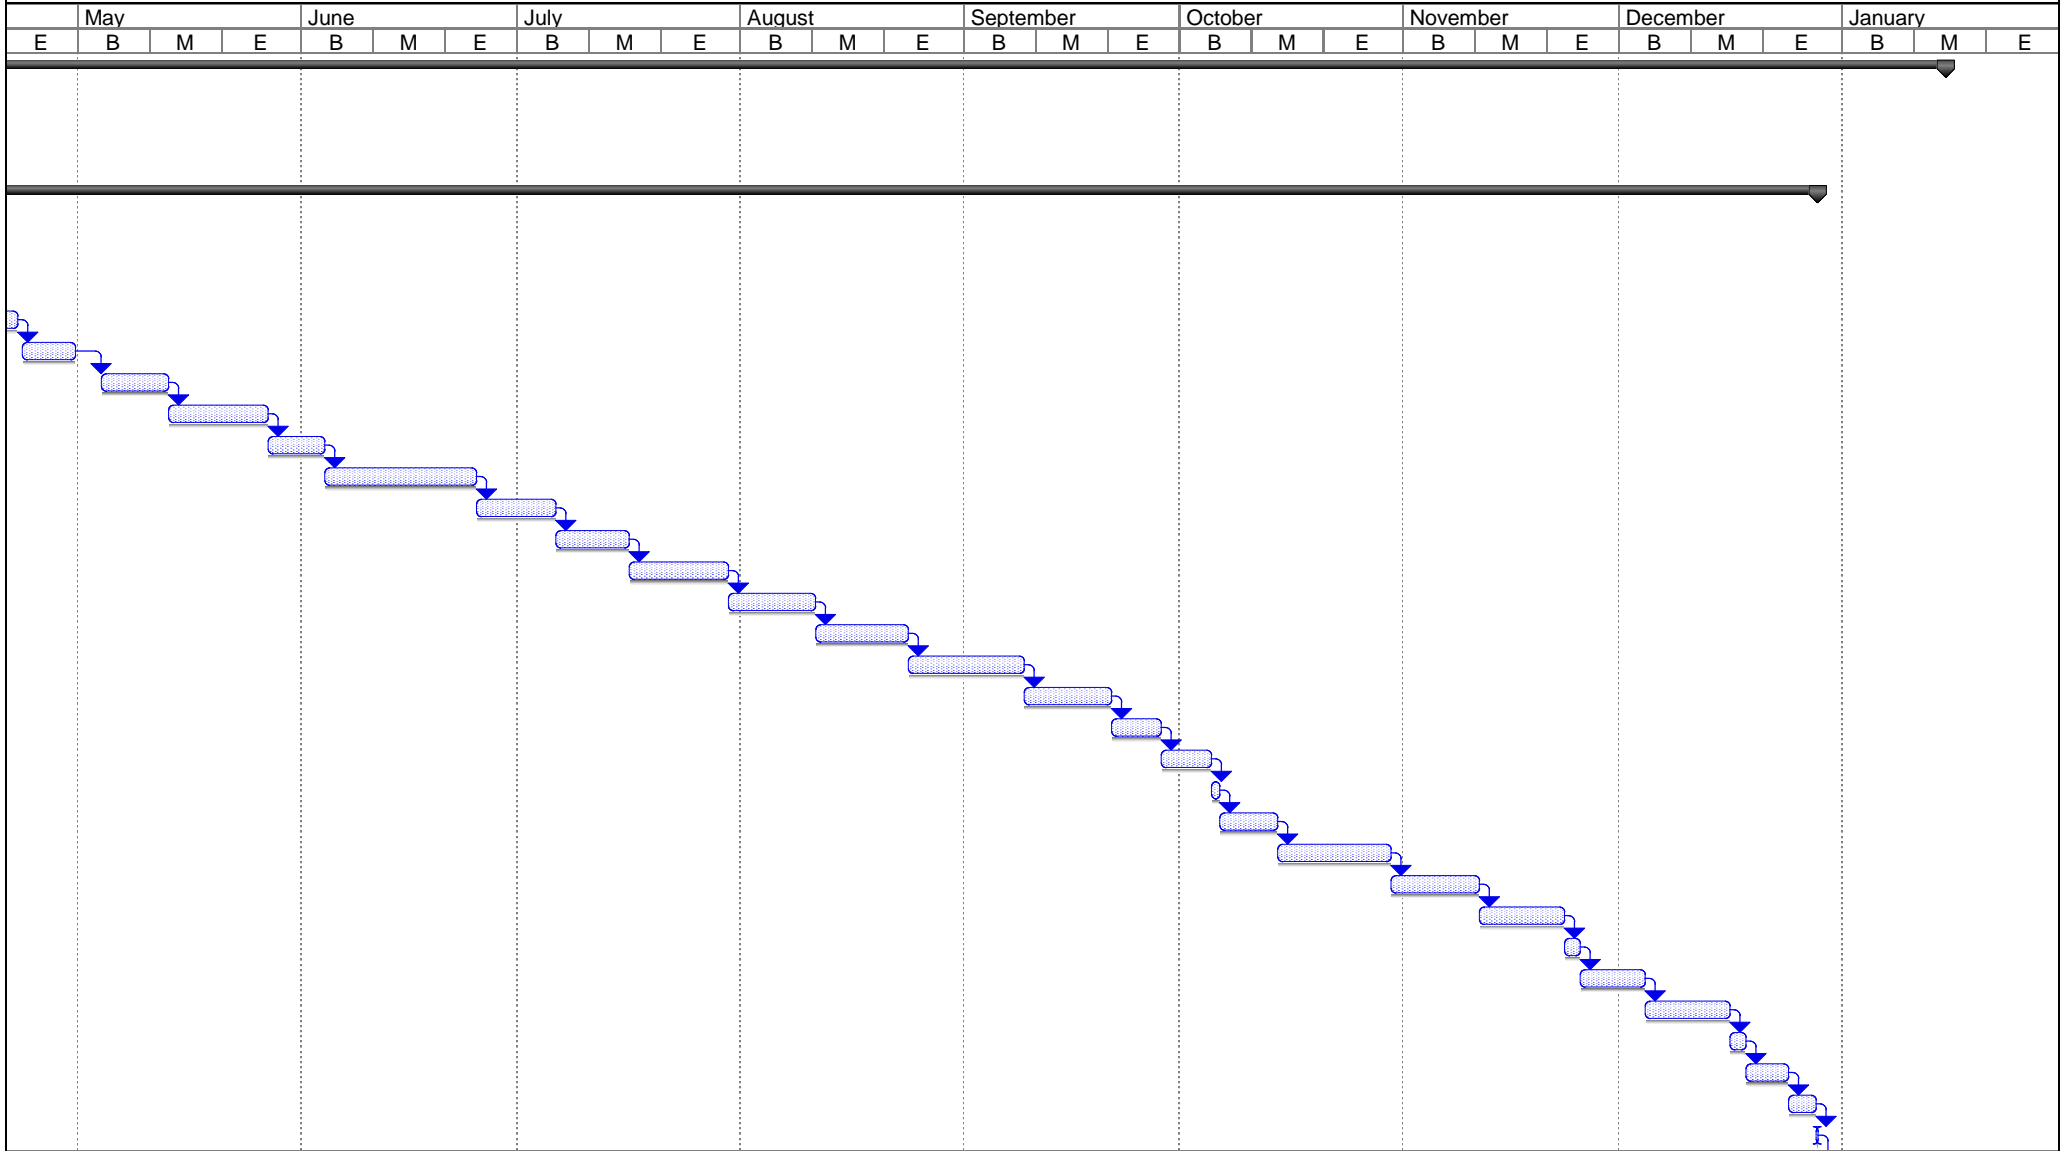

Schedule: 01 - 32mh, 32mh, 16mh
 Date: Thursday, January 08, 2009
 Work Week: Monday thru Thursday

Task		Milestone		External Tasks	
Split		Summary		External MileTask	
Progress		Project Summary		Split	

MANSFIELD UNIVERSITY - LIGHTING RETROFIT INSTALLATION SCHEDULE











Schedule: 01 - 32mh, 32mh, 16mh
 Date: Thursday, January 08, 2009
 Work Week: Monday thru Thursday

- | | | | | | |
|----------|--|-----------------|--|-------------------|--|
| Task | | Milestone | | External Tasks | |
| Split | | Summary | | External MileTask | |
| Progress | | Project Summary | | Split | |

MANSFIELD UNIVERSITY - LIGHTING RETROFIT INSTALLATION SCHEDULE

February				March			April			May			June			July			August			September			October					
E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E









Schedule: 01 - 32mh, 32mh, 16mh
 Date: Thursday, January 08, 2009
 Work Week: Monday thru Thursday

Task		Milestone		External Tasks	
Split		Summary		External MileTask	
Progress		Project Summary		Split	

MANSFIELD UNIVERSITY - LIGHTING RETROFIT INSTALLATION SCHEDULE

February				March			April			May			June			July			August			September			October		
E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E

Schedule: 01 - 32mh, 32mh, 16mh
 Date: Thursday, January 08, 2009
 Work Week: Monday thru Thursday

Task		Milestone		External Tasks	
Split		Summary		External MileTask	
Progress		Project Summary		Split	
